

# Request for Quote

## to Install Customer Supplied Equipment

### Contractor

HVAC Experts  
 456 Chicago Ave  
 Evanston, IL 60202  
 (847) 876-8976

### Questions?

Brian Demoray  
 (800) 865-5931 x368  
[brian.demoray@alpinehomeair.com](mailto:brian.demoray@alpinehomeair.com)

### About This Job

Customer Name	Andrew [to be provided]
Quote ID	PY864789
Document Date	10/31/2016
Location	[to be provided] N. Clybourn, Chicago, IL 60614
Phone Number	[to be provided]

### Customer Supplied Products to Be Installed by You

1		<b>Goodman GSX140241</b> 2 Ton, 14 or 15 SEER Condenser, R-410A Refrigerant
1		<b>Goodman CAPF3636A6</b> 3 Ton, W 14 x H 22 x D 21, Painted Cased Evaporator Coil
1		<b>Rectorseal TO5</b> Kickstart® Hard Start Device
1		<b>Alpine AG-PAD30</b> 30" x 30" x 2" UV Resistant Plastic Condensing Unit Pad
1		<b>Alpine AG-WHP10</b> 1/2 x 48 Inches, #10 Gauge Electrical Whip
1		<b>Alpine AG-DCT</b> Safety Non-Fused Electrical Disconnect

### Comments About This Job

Customer will retain existing linesets, contractor to flush and reuse linesets.

Outside condenser will sit on  
 New condensing pad supplied by customer

Electric breakers required for install  
 30 Amp breaker currently used for existing condenser, new condenser requires 25 Amp breaker

Square footage of the home/building  
 750 Sq foot condo on third floor

Type of home  
 Three story without basement/crawlspace

Electrical circuit panel name brand  
 Siemens

Furnace fuel source  
 Natural Gas

Existing supply plenum dimensions  
 14 inches wide with plenty of space to fit new cased coil

Evaporator coil dimensions (height x width x depth)  
 New coil is 22 x 14 x 21

Air handler/Furnace location  
 Mechanical closet with easy accessibility

Floor drain accessibility  
 Water drain already exists - will connect to that

### Job Site Photos



Front view of 3rd floor condo where products will be installed




Work space for coil install



Existing uncased coil, will be replaced with new cased coil that is perfect fit on top of 14 inch wide furnace



Existing 30 Amp breaker for current condenser

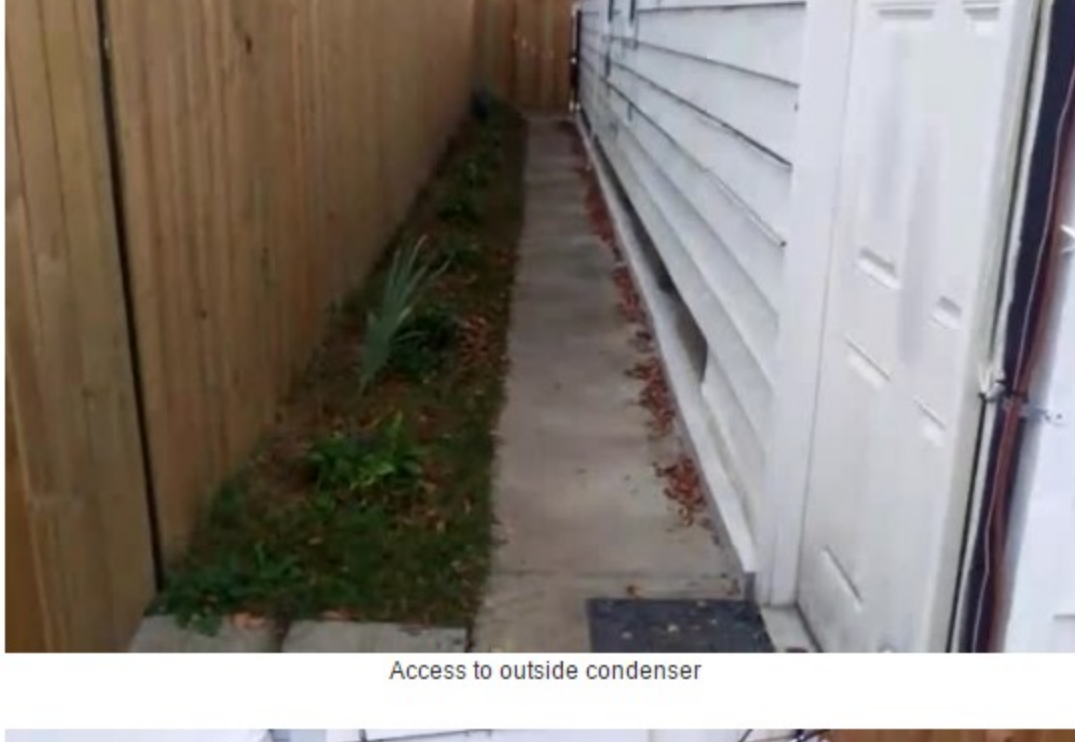

Access to outside condenser



Work space for condenser replacement



Condenser that will be replaced



Existing disconnect that will be replaced

### Contractor

HVAC Experts  
 456 Chicago Ave  
 Evanston, IL 60202  
 (847) 876-8976

### Your work to include

- ✓ Installation of all listed customer supplied equipment / products (provided by customer, not contractor)
- ✓ Removal and environmental disposal of old equipment
- ✓ Perform installation in workmanlike manner according to code
- ✓ Obtaining applicable local permits as necessary
- ✓ Providing misc. materials and supplies needed to complete installation (wire, breaker, pipe, screws, etc.)
- ✓ Start up and inspection for proper performance
- ✓ Clean up of job site when finished
- ✓ One year labor warranty (product includes MFR warranty on parts)
- ✓ Operating as licensed, independent contractor working for end-user customer, not an employee or partner of Alpine
- ✓ Carry workers compensation insurance for contractors' employees as well as business liability insurance

### Enter your price to do this job

[Why this job is more profitable](#)

\$

### Enter your earliest available installation date

### Comments to customer (optional)

### Type your name to sign

X

[Submit My Bid](#)

[No thanks, I'm not interested in this job.](#)

### What happens next

If your bid is accepted by customer, we will contact you to schedule installation date and provide complete customer info. When you have completed the job, payment will be made to you by Alpine via check for the amount you entered above (minus 2.5% transaction fee) within 10 days of job completion.
